VENDORGATE

Vendor Onboarding and Purchase Order Portal

Project Planning Documentation

Case Study No. 88

Field	Details
Document Name	VendorGate Project Plan
Project	VendorGate – Vendor Onboarding & Purchase Order Approval Portal
Document Type	Project Planning Documentation
Version	1.0
Status	Submission Draft
Planning Basis	Case-study task durations and dependencies

1. Project Overview

VendorGate is a proposed centralized portal for managing vendor registration and purchase-order approval for a mid-size pharmaceutical distributor. This project plan organizes the supplied activities, dependencies, schedule logic, critical path, float, milestones and the effect of approval-policy delays.

This document complements the BRD, SOW and SRS and does not replace their requirements or business rules.

2. Project Planning Objectives

- Create a structured schedule using the exact case-study activities, durations and dependencies.
- Identify dependent activities and the critical path.
- Calculate float for non-critical activities.
- Assess the impact of a delayed approval-limit policy decision.
- Define milestones as zero-duration checkpoints.
- Provide a Gantt-style schedule for project monitoring.
- Establish a basis for tracking progress and delays.

3. Planning Approach

The project uses dependency-based scheduling. A successor activity starts only after its required predecessor activities are completed. Project-relative days are used; Day 1 represents project start.

4. Work Breakdown Structure

WBS ID	Activity	Duration	Predecessor
1.1	Requirements	8 days	—
1.2	Approval-limit policy sign-off	6 days	Requirements
1.3	Vendor registration module	14 days	Requirements
1.4	PO module	16 days	Approval-limit policy sign-off
1.5	Vendor acknowledgement	6 days	PO module

1.6	Testing	8 days	Vendor registration module + Vendor acknowledgement
1.7	Vendor onboarding drive	15 days	Testing

5. Task Dependency Analysis

Activity	Depends On	Dependency Meaning
Requirements	None	The project starts with requirements.
Approval-limit policy sign-off	Requirements	Approval rules are finalized after requirements.
Vendor registration module	Requirements	Registration work starts after requirements.
PO module	Approval-limit policy sign-off	PO workflow depends on approved limits.
Vendor acknowledgement	PO module	Acknowledgement follows the PO workflow.
Testing	Vendor registration + Vendor acknowledgement	Testing waits for both required workstreams.
Vendor onboarding drive	Testing	Onboarding starts after testing.

6. Schedule Calculation

A standard forward-pass/backward-pass calculation is used. Early Finish = Early Start + Duration − 1. Float = Late Start − Early Start.


Activity	Dur.	Pred.	ES	EF	LS	LF	Float
Requirements	8	—	1	8	1	8	0
Approval-limit policy sign-off	6	Requirements	9	14	9	14	0
Vendor registration module	14	Requirements	9	22	23	36	14
PO module	16	Policy sign-off	15	30	15	30	0
Vendor acknowledgement	6	PO module	31	36	31	36	0
Testing	8	Vendor registration + acknowledgement	37	44	37	44	0
Vendor onboarding drive	15	Testing	45	59	45	59	0

7. Critical Path

Requirements → Approval-Limit Policy Sign-off → PO Module → Vendor Acknowledgement → Testing → Vendor Onboarding Drive

Critical Path Duration: 59 project days

The critical path consists of activities with zero float. Based on the supplied durations and dependencies, the critical path is Requirements → Approval-Limit Policy Sign-off → PO Module → Vendor Acknowledgement → Testing → Vendor Onboarding Drive, with a total planned duration of 59 project days.

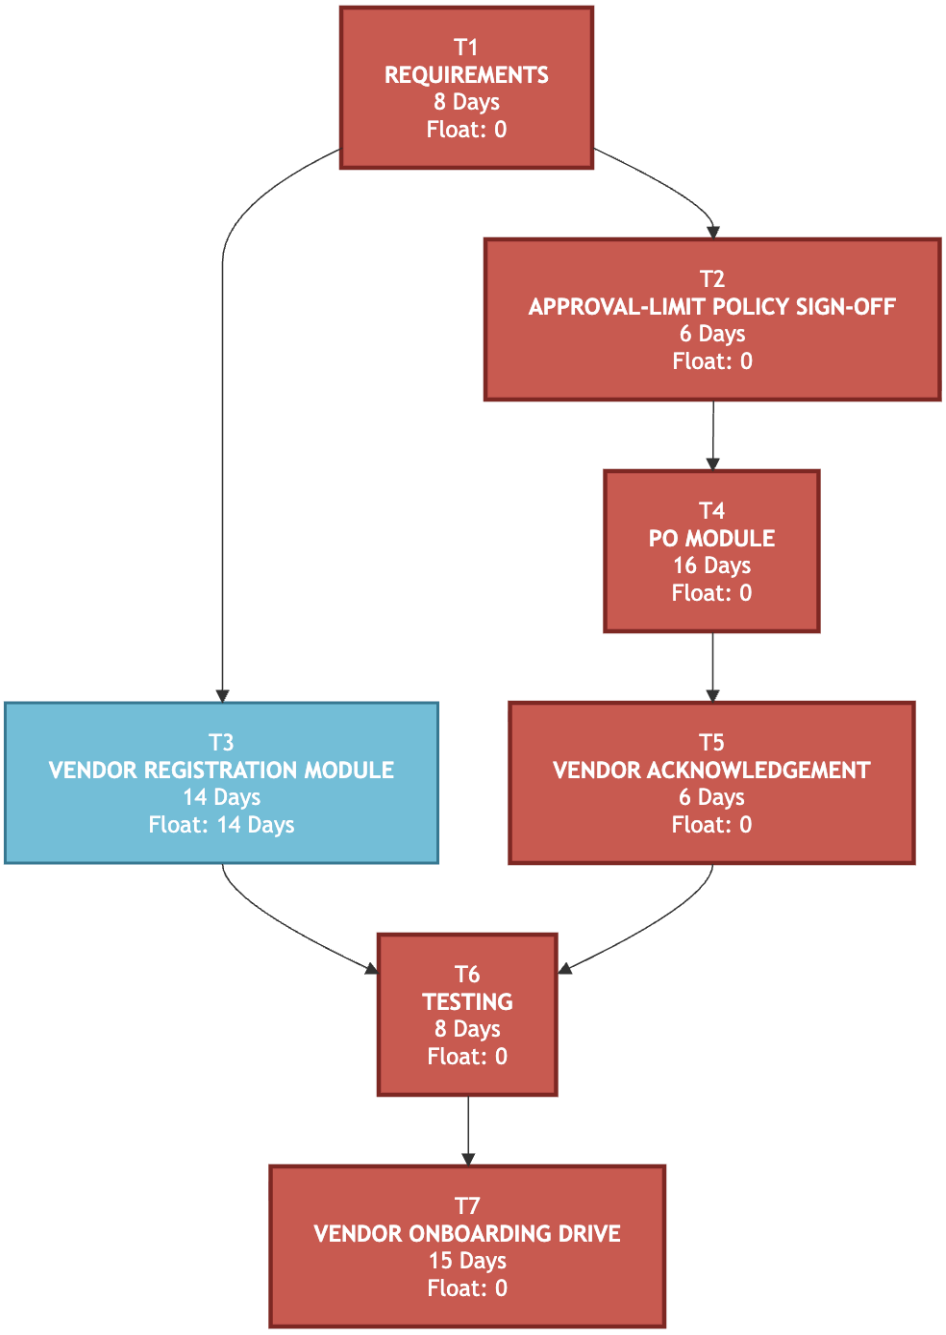

8. Float Analysis

Activity	Float	Planning Interpretation
Requirements	0 days	Delay directly affects project completion.

Approval-limit policy sign-off	0 days	Critical-path activity; delay affects downstream activities.
Vendor registration module	14 days	Can be delayed by up to 14 days without delaying Testing, assuming the critical path remains on schedule.
PO module	0 days	Critical-path activity; delay affects Vendor Acknowledgement.
Vendor acknowledgement	0 days	Critical-path activity; delay affects Testing.
Testing	0 days	Delay affects Vendor Onboarding.
Vendor onboarding drive	0 days	Final activity; delay extends project completion.

9. Impact of Delayed Approval-Limit Policy Decision

Scenario	Effect
No delay	PO workflow proceeds according to the planned schedule.
Any delay in policy sign-off	Since policy sign-off is on the critical path, the delay can shift the PO Module and all dependent activities.
Policy delay + other delays	Combined delays can extend the overall project completion further.


The Approval-Limit Policy Sign-off activity has **0 days of float** because it lies on the critical path. Therefore, a delay in policy sign-off can directly affect the PO Module, Vendor Acknowledgement, Testing and Vendor Onboarding Drive.

10. Gantt-Style Project Schedule

Activity	Day Range	Duration
Requirements	1–8	8 days

Approval-limit policy sign-off	9–14	6 days
Vendor registration module	9–22	14 days
PO module	21–36	16 days
Vendor acknowledgement	37–42	6 days
Testing	43–50	8 days
Vendor onboarding drive	51–65	15 days

The day ranges are project-relative and can be converted into calendar dates once an approved project start date is available.

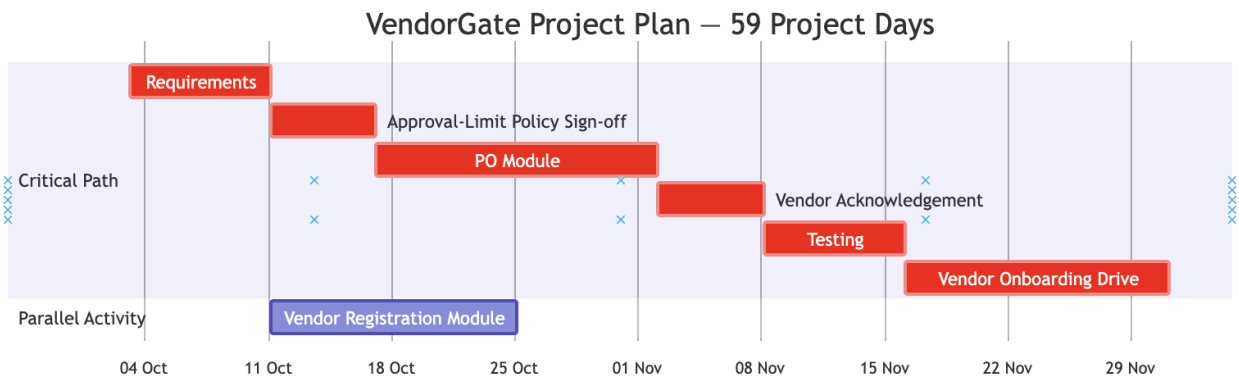

11. Project Milestones

Milestone	Checkpoint	Timing
M1	Requirements completed	End of Day 8

M2	Approval-limit policy sign-off completed	End of Day 14
M3	Vendor registration module completed	End of Day 22
M4	PO module completed	End of Day 30
M5	Vendor acknowledgement completed	End of Day 36
M6	Testing completed	End of Day 4
M7	Vendor onboarding drive completed	End of Day 59

Milestones are zero-duration checkpoints, not additional work activities.

12. Project Monitoring & Control

- Track actual completion against planned day ranges.
- Verify predecessor completion before starting dependent tasks.
- Monitor approval-limit policy sign-off closely.
- Track zero-float activities as schedule-sensitive.
- Record delays and their downstream impact.
- Recalculate float and critical path after material schedule changes.
- Use milestone completion as formal progress checkpoints.

13. Schedule Change Control

Change Type	Required Planning Check
Duration change	Recalculate early/late dates and float.

Dependency change	Recalculate dependency network and critical path.
Approval-policy change	Assess PO routing and downstream schedule impact.
Scope change	Assess new activities, durations and dependencies.
Delay	Record actual delay and assess successor impact.

14. Planning Assumptions & Constraints

- No project start date is supplied; therefore project-relative days are used.
- Task durations are treated as the case-study planning durations.
- Dependencies are treated as finish-to-start relationships unless otherwise stated.
- Testing starts only after both vendor registration and vendor acknowledgement are complete.
- Milestones have zero duration.
- No additional activities are inserted into the critical-path calculation.

15. Case-Study Requirement Mapping

Required Planning Item	Covered In
Task dependencies	Section 5 – Task Dependency Analysis
Critical path	Section 7 – Critical Path
Float for non-critical activities	Section 8 – Float Analysis
Impact of delayed approval-policy decision	Section 9
Gantt chart / schedule	Section 10 – Gantt-Style Project Schedule
Milestones	Section 11 – Project Milestones

16. Planning Summary

The VendorGate project plan organizes the case-study activities into a dependency-based schedule. Under the supplied durations and dependencies, the planned project duration is **59 project days**. The critical path is **Requirements → Approval-Limit Policy Sign-off → PO Module → Vendor Acknowledgement → Testing → Vendor Onboarding Drive**. The Vendor Registration Module has **14 days of float**, while the activities on the critical path have **0 days of float**.
